



Montezuma-Cortez
High School



DAT Design Meeting

November 12, 2013

Meeting Agenda


- Schedule and budget update
- FF&E selection
- Review site
- Design development user comments
- LEED/Sustainability
- Next steps

Schedule Update

- Bid Package #1 due Nov. 14 (grading & drainage)
- Bid Package #2 due Dec. 16 (foundations)
- Bid Package #3 due Jan. 22 (remainder of building and site)
- Site work scheduled to begin in December
- Ground Breaking (and Blessing) on Dec. 21 (winter solstice)

Budget Update

- The current MACC is \$33,918,000
- Current budget estimate is at approx. \$34.2M
- The design and construction team are working to find savings to close this gap within the next 3-4 weeks.
- Additional savings continue to be identified going forward

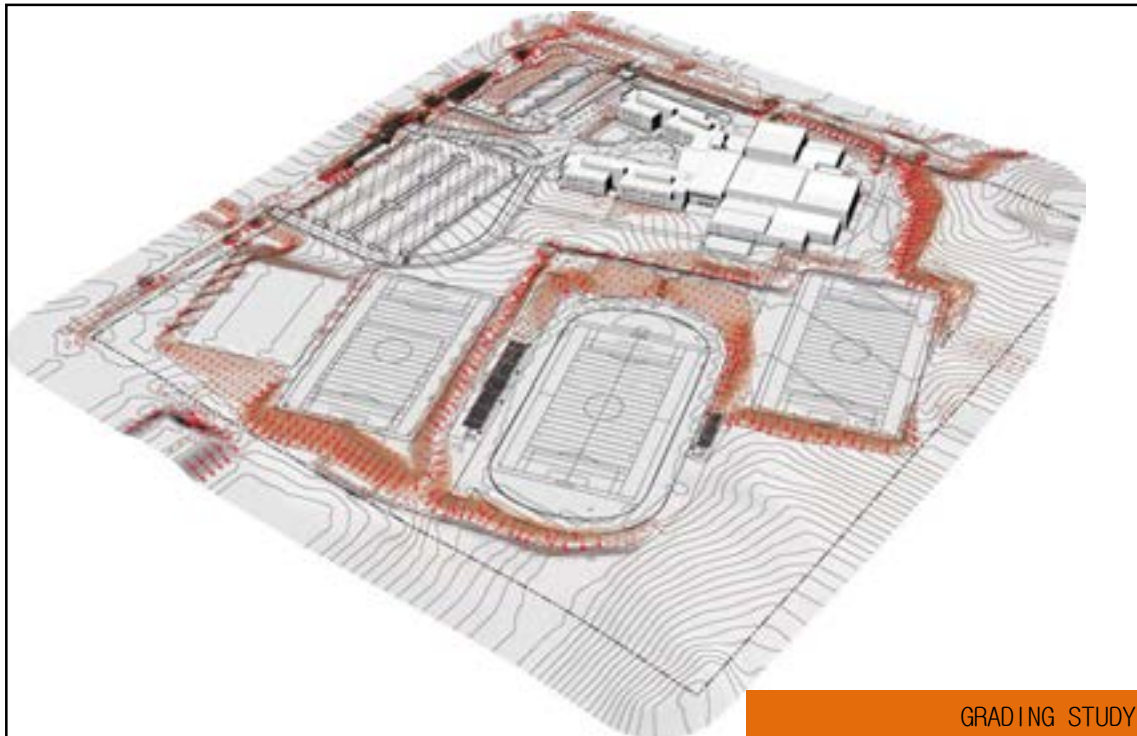

Design Development User Comments


- Common's stair
- Science classrooms
- Administration
- Health services
- Site circulation





Common's stair comments

- Wall blocked view
- Stair too closed off
- Can it move?
- Can it be split into 2 stairs and moved to the ends?

DD USER COMMENTS

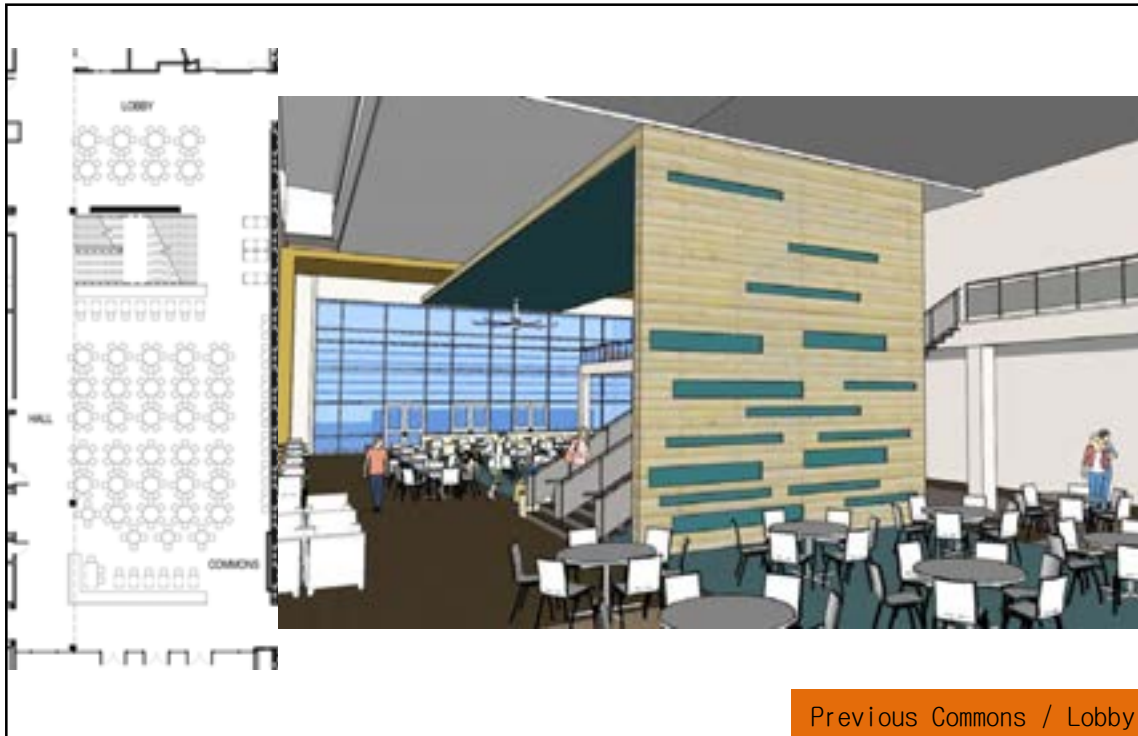

Previous Commons / Lobby

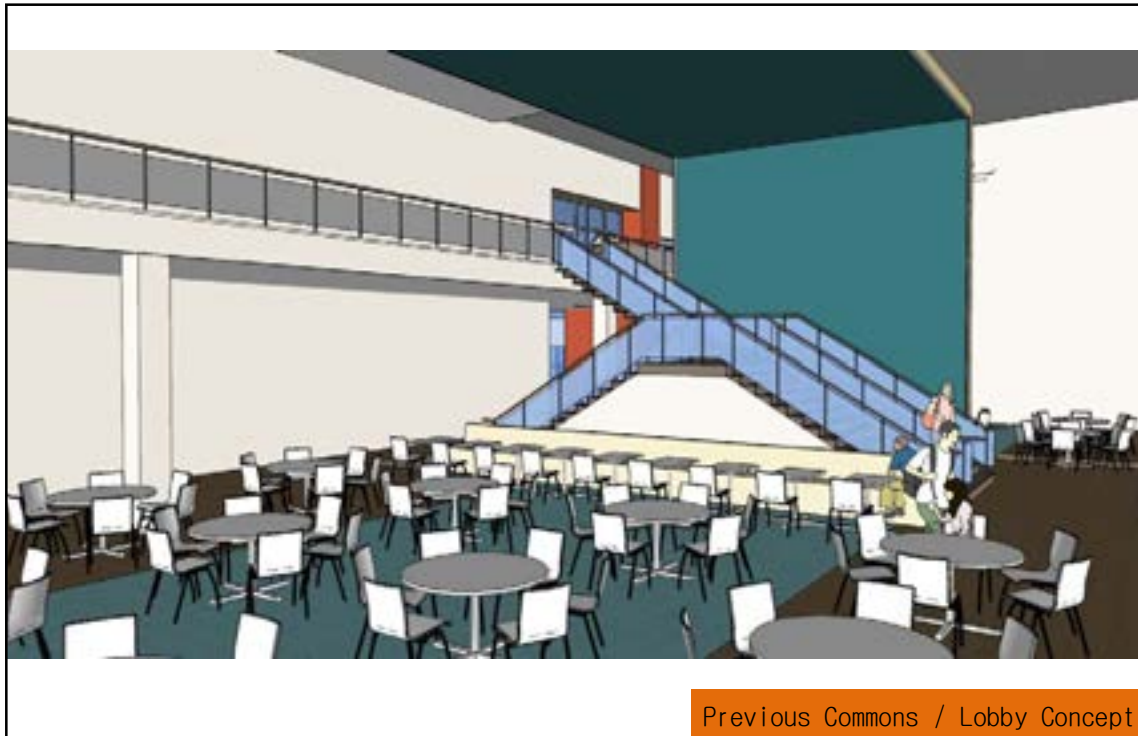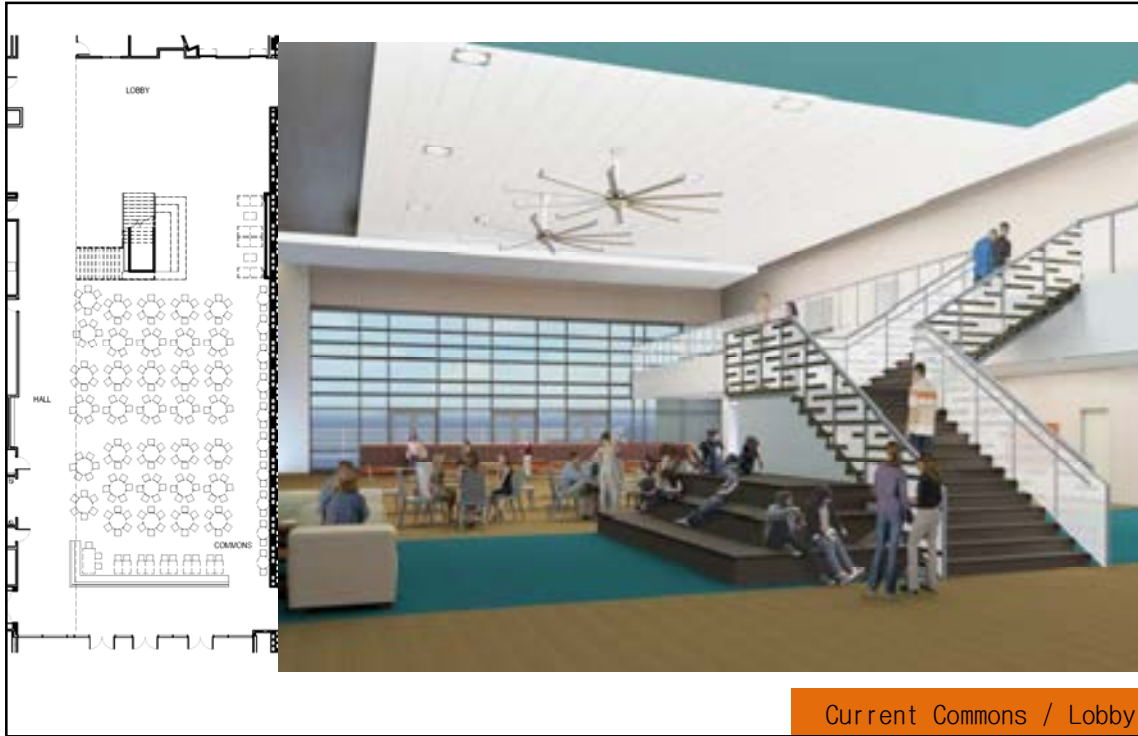



Next Steps...

- Board/Public update tonight
- Bid Package #1 due Friday
- 50% Construction Documents beginning of December
- Bid Package #2 due 12/16 – foundation design
- Do we need a DAT meeting in Dec...?
